First & Final bill

Recorded on:-

Job Number: 004-21-000028

M. A. R. 57 (Rule 116)

Measurement Book

No. E

Serial No. 497409

Name of work Additional and Alteration of School Building at Kamakanagara, Allalasandra and Ambedkarnagara in ward no-04.

Name of Contractor or nature of Agency Sri Rajhuraatha B.P, M/S Goutham Construction, #47, 2nd main, muneshwara layout, Lagere, Near outer Ring Road, Bangalore-560058.

Date of commencement of work

Modified Cost RS. 102.75 Lakhs

work order no:- BBMP/EE/YNK.D/EPMT-14/W.O/84/2021-22 Date 28/01/2022

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (1) KSRRB m200-12.3. Dismantling of existing structures like culverts bridges, retaining walls and other structure comprising of masonry, Cement Concrete, wood work, steel work, including T&P and Scaffolding wherever necessary etc as per Specifications. | | | | | | |
| | Quantity vide, As per prepared in excel sheet:- 65.80 $m^3$ | | | | | | |
| | | | | | | CRS. 1800.21 | 118450.53 |
| | (2) KSRRB m200-14.2. Dismantling of existing structure like culverts, bridges, retaining walls and other structure comprising of masonry, Cement Concrete, wood work, steel work, | | | | | | |

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | including T & P and Scaffolding wherever necessary cleared Per Specifications. Quantity vide, AS per prepared in excel sheet:- 81.98 $m^3$ @Rs. 397.65 | | | | | | 32599.94 |
| (3) | 37.51: Dismantling Cement Concrete flooring or plain Cement Concrete work including removing and Conveying the debries to distance up to 200m (within average Thickness of 15cms) cleared per Specifications. Quantity vide, AS per prepared in excel sheet:- 264.68 $m^2$ @Rs. 97.43 | | | | | | 25788.02 |
| (4) | Dismantling plastering and removing the debries with a | | | | | | |

Serial No. .....
Name of work .....
Name of Contractor of nature of Agenc
Date of commencement of work.....

| Date | Full description, etc, of work |
|---|---|
| 1 | 2 |
| | lead up to 200m Quantity vide, AS |
| (5) | Conveying the c... with including ... Per the direction ... Quantity vide, AS |

M. A. R. 57 (Rule 116) No. E 497410
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Lead up to 200m. etc as per Specifications. Quantity vide, AS per prepared in excel sheet:- 451.79 $m^2$ CRS. 41.92 | | | | | | 18939.04 |
| | (5) Conveying the excavated earth, debries etc, with all lead and lifts including loading and unloading charges etc. Complete as per the direction of the engineer in-charge. Quantity vide, AS per prepared in excel sheets:- 269.21 $m^3$ CRS. 70.38 | | | | | | 18947.27 |

M. A. R. 57 (Rule 116)
Measurement Book

No. E
497411

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Number | Dimensions: Length | Dimensions: Breadth | Dimensions: Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Quantity vide, AR per prepared in excel sheets:- | | | | | 19.35 $m^3$ | |
| | | | | | CRS. | 2757.86 | 53,248.49 |
| | (8) KSRB 4-1.6: Providing and laying in position plain Cement Concrete of mix 1:2:4 with Cement @ 401 kgs, with 20mm and down Size graded granite metal Coarse aggregates @ 0.69 cum and fine aggregates @ 0.459 cum machine mixed etc as per Specifications. | | | | | | |
| | Quantity vide, AR per prepared in excel Sheet:- | | | | | 46.90 $m^3$ | |
| | | | | | CRS. | 6706.56 | 3,14,539.01 |
| | (9) KSRB 4.1.5: Providing and laying in position plain Cement Concrete | | | | | | |

**M. A. R. 57 (Rule 116)** No. E 497412
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency. .....
Date of commencement of work. .....

| Date | Full description, etc, of work | Number | Dimensions: Length | Dimensions: Breadth | Dimensions: Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Quantity vide, AS per prepared in excel sheet:- 59.70 m³ CRS. 5206.90 | | | | | | 3,10845.42 |
| | (11) KSRB 2.3: Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20cms in depth Compacting each deposited layer by rammering after watering with lead upto 50mm etc as per Specification. | | | | | | |
| | Quantity vide, AS per prepared in excel sheet:- 170.71 m³ CRS 227.72 | | | | | | 38,874.99 |
| | (12) KSRB 4-6.1: Providing and removing Centering, shuttering, strutting | | | | | | |

M. A. R. 57 (Rule 116)
Measurement Book

No. E 497413

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Number | Dimensions: Length | Dimensions: Breadth | Dimensions: Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| (14) | KSRB 4-6.5: Providing and removing Centering, Shuttering, Struting propping etc and Removal of form work for Columns, pillars piers, post and Struts, Square/ rectangular/polygon in plain including cost of all materials, labour complete as per Specifications. Quantity vide, As per prepared in excel sheet: 187.49 m² DRS 516.61 | | | | | | 96,858.18 |
| (15) | KSRB 4-6.2: Providing and removing Centering shuttering, Strutting propping etc.. and removal of formm work for | | | | | | |

M. A. R. 57 (Rule 116) No. E 497414
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Number | Dimensions: Length | Dimensions: Breadth | Dimensions: Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (17) KSRB 4-6.7: Providing and removing Centering, Shuttering, Struttings propping etc. and removal of formwork for Sides and Soffits of beams, beams haunchings, Cantilever girders, brackets and lintels not exceeding 1m in depth including cost of all materials, labour Complete as per Specification. Quantity vide, As per prepared in excel sheet: -242.57m² | | | | | CR8. 330.81 | 80,242.93 |
| | (18) KSRB 4-6.11 Providing and removing Centering, Shuttering, Struttings propping etc and removal of formwork for Stairs (excluding landing) except Spiral Staircase including cost of all materials | | | | | | |

M. A. R. 57 (Rule 116) No. E 497415
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Number | Dimensions Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | gates @0.70 cum and fine aggregates @0.47 cum. with Super plasti cizers @3 Lts Conforming to IS 9103-1999 reaffirmed-2008 at machine mixed cleaned as per specification. Quantity vide, AS per prepared in excel sheet:- 88.84 m³ CRS. 738334 | | | | | 6,55,961.77 | |
| (21) | KSRB 4.2.8: Providing and laying in position reinforced Cement Concrete of design mix m25 with opc Cement @340 Kgs, with 20mm and down size graded granite emetal coarse aggregates @0.70 cum and fine aggregates @0.47 cum, with Superplasticiser @3 Lts Conforming to IS 9103-1999 Reaffirmed 2008 cleaned as per Specification. G.F, | | | | | | |

M. A. R. 57 (Rule 116)
Measurement Book

No. E 497416

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

| Date | Full description, etc, of work | Number | Dimensions: Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (23) Providing and laying Cement Concrete using 20mm and down size granite aggregates and fine aggregates of ready mixed Concrete (Rmc) for Rcc works laid in 15cms Thick layers and well Compacted including vibrating Compacted as per Specifications G.F. | | | | | | |
| | Quantity vide, As per prepared in excel sheet:- 79.06m³ @Rs. 7026.47 | | | | | 5,55,521.50 | |
| | (24) KSR 4.2.11: Providing and laying in position reinforced Cement Concrete of design mix m20 with opc Cement @ 27.20Kgs with 12mm and down size graded granite metal Coarse | | | | | | |

M. A. R. 57 (Rule 116) No. E
Measurement Book

497419

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

| Date | Full description, etc, of work | Number | Dimensions: Length | Dimensions: Breadth | Dimensions: Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (31) KSRB 15.3.8: Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering etc all per specification. F.F. | | | | | | |
| | Quantity vide, AS per prepared in excel sheet:- | | | | | 631.99 $m^2$ | |
| | A) up to 125 % of Qty:- | | | | | 358.51 $m^2$ | |
| | @RS. 309.29 | | | | | | 110,884.33 |
| | B) Above 125 % of Qty:- | | | | | 273.48 $m^2$ | |
| | @RS. 302.49 | | | | | | 82,724.21 |
| | (32) KSRB 15.3.2: Providing 12mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off | | | | | | |

M. A. R. 57 (Rule 116) No. E
Measurement Book

497421

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work.....

| Date | Full description, etc, of work | Number | Dimensions Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (37) KSRB 15-15.1: Providing and applying painting in two coats with plastic emulsion paint of approved brand on wall surface to give an even approved shade after thoroughly brushing the surface, free from mortar drops and other foreign matter including preparing the surface even and hard papers etc as per Specification. Quantity vide As per prepared in excel sheet: - | | | | | 635.60 m² | 64,805.27 |
| | | | | | | CRS. 101.96 | |
| | (38) KSRB 15-14.1: Providing and applying two coats with oil bound washable distemper of approved brand and shade on wall surface including priming coat with distemper primer after | | | | | | |

M. A. R. 57 (Rule 116) No. E
Measurement Book

497423

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Number | Dimensions Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | 50mm Thick with metallic Concrete hardner topping under layer of 35mm Thick m-15 cement Concrete using broken granite metal of 20mm and down size. and top layer 50mm Thick of metallic Cement hardner Con - Sisting of mix 1:2 (1 cement : 2 granite metal 10mm nominal size) ck of per specification. F.F, | | | | | | |
| | Quantity vide, AS per prepared in excel sheet :- | | | | | 194.44 m² | |
| | A) up to 125% of quantity :- | | | | | 103.13 m² | 73,955.06 |
| | | | | | C.R.S. | 717.14 | |
| | B) Above 125% of quantity :- | | | | | 91.31 m² | 65,482.05 |
| | | | | | C.R.S | 717.14 | |

**M. A. R. 57 (Rule 116)** No. E 497424
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | A) up to 125% of quantity:- | | | | | 114.49 m² @Rs. 1108.00 | 126852.15 |
| | B) Above 125% of quantity:- | | | | | 91.34 m² @Rs. 1108.00 | 101207.49 |
| 45 | KSRB 14-14.5: Providing ceramic tiles of approved make shade and size for flooring treads of steps and landings laid on bed of 12mm thick cement mortar 1:3 mix, flush pointing with white cement using colour pigment as per specifications quantity vide AS per prepared in excel sheet:- 1.80 m² | | | | | @125 1370.83 | 2467.49 |

**M. A. R. 57 (Rule 116)** No. E 497426
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | windows, ventilators and other frames, wrought framed or assembled including making plaster grooves deals per Specification. G.F, Quantity vide, AR per prepared in excel sheet - 0.39 $m^3$ @Rs. 99248.32 | | | | | 38,587.75 | |
| (51) | KSRB 9.4-2: Providing Home wood frames of doors, windows, clere story window, ventilators and other frames, wrought framed or assembled including making plaster grooves deals per Specification. F.F, Quantity vide, AR per prepared in excel sheet:- 0.65 $m^3$ | | | | | | |

**M. A. R. 57 (Rule 116)** No. E 497427
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Number | Dimensions Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Home wood shutters for doors, styles and rails of 40mm. Thick with bottom and lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25mm Thick including Cost of materials labour, Hire of machineries Complete as per Specifications. | | | | | | |
| | Quantity vide, AB, per prepared in excel sheet - 6.30 $m^2$ @Rs. 5349.65 | | | | | 33702.80 | |
| (54) | KSRB 9.5-2: Providing and fixing in position fully panelled Homewood shutters for doors, styles and rails of 40mm Thick with bottom & lock panels of 25mm Thick Cleod per specifications. | | | | | | |

M. A. R. 57 (Rule 116)
Measurement Book

No. E
497429

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

| Date | Full description, etc, of work | Number | Dimensions Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (59) Providing and fixing ms grill work for windows and ventilato-rs weighing 21 kgs/ Sqm, using ms flats or ms Square bars or Combination of ms flats and square bars as per approved design, drawing including cutting steel Sections and welding the same to required pattern with a Coat red lead primer & two coats Synthe tic enamel paint etc as per Specifications. | | | | | | |
| | Quantity vide, As per prepared in excel Sheet:- | | | | | 378.00 kgs | |
| | | | | | @Rs. | 107.53 | 40,646.34 |
| | (60) Providing and fixing ms grill work for windows and ventilators | | | | | | |

M. A. R. 57 (Rule 116) No. E
Measurement Book

497430

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|
| | | Number | Length | Breadth / Depth | | |
| 1 | 2 | 3 | 4 | 5 / 6 | 7 | 8 |
| | Quantity vide, AS per prepared in excel sheet:- | | | | 148.23 m² | |
| | A) upto 125% of Quantity:- @R.S. 107.63 | | | | 119.25 m² | 12834.88 |
| | B) Above 125% of Quantity:- @R.S. 107.63 | | | | 28.98 m² | 3119.12 |
| (62) | KSRRB m300 - Construction of embankment with material Gravelly murrum. KSRRB m300.5a. Construction of embankment with approved material grading to required slope and Compacting to meet require | | | | | |

M. A. R. 57 (Rule 116) No. E

Measurement Book

497432

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (67) Concealed Conduit System - Supplying heavy guage pvc Conduitpipe ....mm dia.....mm Thick Confirming to IS 2509 with Suitable Size bends, metal/pvc Junction boxes etc as per Specifications. Quantity vide, AS per prepared in excel sheet. - 55.00 mtrs CRS. 55.60 | | | | | | 3058.00 |
| | (68) Groove cutting :- Supplying heavy guage Conduit pvc 25/2mm of S Thick heavy with Suitable Size bends metal Junction boxes, adhesive particle as per Specifications. 19/20mm Dia, 2mm Thick. Quantity. AS per prepared in excel sheet :- 12.00 mtrs CRS. 53.50 | | | | | | 642.00 |

M. A. R. 57 (Rule 116)
Measurement Book

No. E 497434

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|
| | | Number | Length | Breadth / Depth | | |
| 1 | 2 | 3 | 4 | 5 / 6 | 7 | 8 |
| | Quantity vide, AR per prepared in excel sheet:- | | | | 12.00 nos | |
| | | | | | @RS. 203.57 | 2442.12 |
| | (75) Supply and fixing of bakelite D.P/ Socket/switch with/ without neon indicator over existing wood board on flush mounting in plastic plate/ switches as per IS 1293 and IS 3854. 16 Amps Combined switch and socket with indication etc as per Specification. | | | | | |
| | Quantity vide, AR per prepared in excel sheet:- | | | | 12.00 nos | |
| | | | | | @RS 157.35 | 1888.20 |
| | (76) wiring for lighting/ power Circuit using one of FRLS pvc insulated | | | | | |

M. A. R. 57 (Rule 116) No. E 497436
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

| Date | Full description, etc, of work | Number | Dimensions Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | | | Add 12% of GST charges RS:- | | | | 10,97,911.46 |
| | | | Grand Total Amount RS:- | | | | 1,02,47,173.65 |

CERTIFICATE:-

1) Certified that the above work done is Satisfactory Completed.
2) Certified that the there is no debrises have been cleared to Site.

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಜ.ಜ.ಎಂ.ಕಿ. ಬೆಂಗಳೂರು-106

21/07/2022

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |

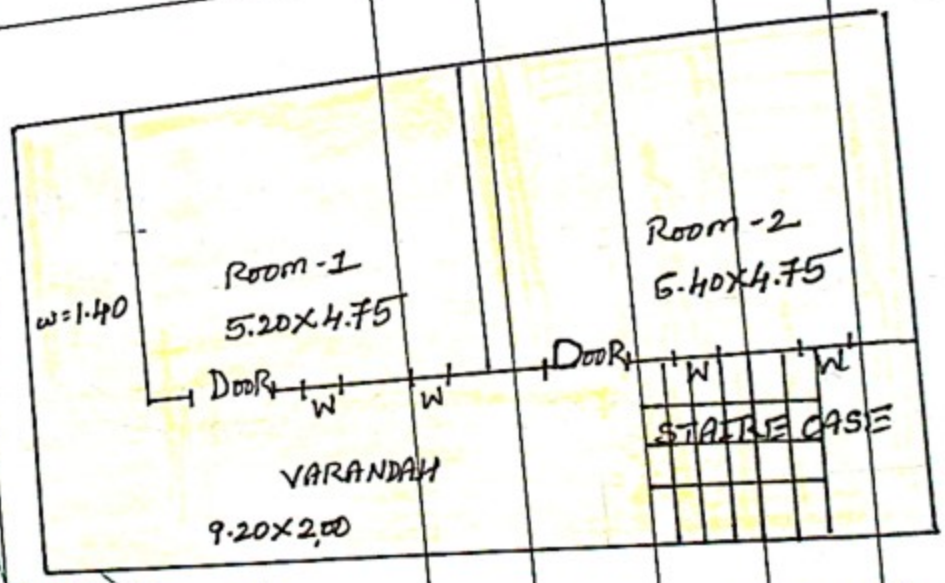


ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಡಿ.ಎ. ಬೆಂಗಳೂರು-10

KANAKANAGARA SCHOOL BUILDING :- [GF & FF]

GL

**M. A. R. 57 (Rule 116)** No. E 497437
Measurement Book

Serial No. ..... From ..... To .....
Name of work .....
Name of Contractor of nature of Agency. .....
Date of commencement of work .....

| Date 1 | Full description, etc, of work 2 | Number 3 | Dimensions Length 4 | Breadth 5 | Depth 6 | Contents 7 | Reference to last Measurement 8 |
|---|---|---|---|---|---|---|---|
| | | | | | | | |

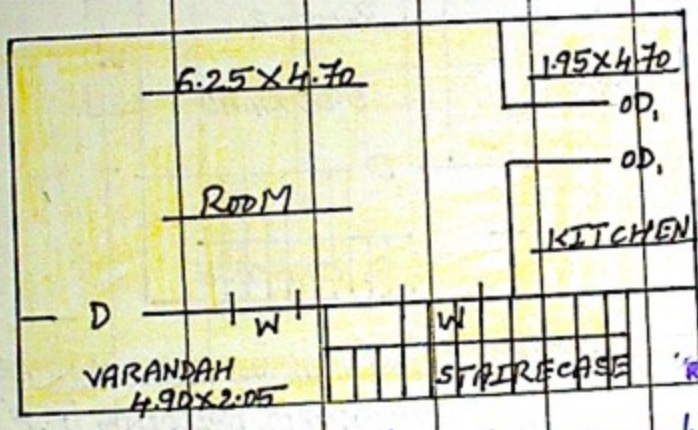


ii) Ambedkar Colony Anganawadi (ಕಿರಿಯ)

GGL

GF&FF

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |

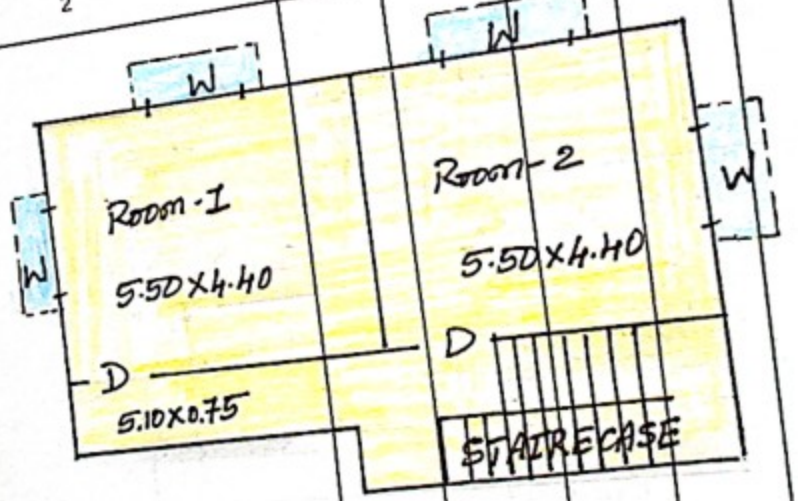


iii) ALLALASANDRA SRISHAKTHI BHAVANA NEAR ANGANAWADI BUILDING [F.F]

ಸಹಾಯಕ ಕಾರ್ಯ ಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಜಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106

AOR

Serial No.
Name of work
Name of Contractor of nature of Agency
Date of commencement of work

| Date | Full description, etc, of work |
|---|---|
| 1 | Bill Amount 9,14,926=00 |
| | (+) GST 1097911=00 |
| | TOTAL 10247000=00 |
| | Less |
| | ITax 102470=00 |
| | SGST 91493=00 |
| | CGST 91493=00 |
| | BOWWC 102470=00 |
| | CBF 102470=00 |
| | ROYALTY 127300=00 |
| | FINE — |
| | FSD — |
| | OTHERS — |
| | TOTAL DEDUCTION 525473 |
| | 9721527=00 |

**M. A. R. 57 (Rule 116)** No. E 497438
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

| Date | Full description, etc, of work | Number | Dimensions: Length | Dimensions: Breadth | Dimensions: Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | Bill Amount 9149262=00 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (+) GST 1097911=00 | | | | | | |
| | TOTAL 10247000=00 | | | | | | |
| | Less I Tax 102470=00 | | | | | | |
| | SGST 91493=00 | | | | | | |
| | CGST 91493=00 | | | | | | |
| | BCWWC 102470=00 | | | | | | |
| | CBF 10247=00 | | | | | | |
| | ROYALTY 127300=00 | | | | | | |
| | FINE — | | | | | | |
| | FSD — | | | | | | |
| | OTHERS — | | | | | | |
| | TDS DEDUCTION 525473=00 | | | | | | |
| | 9721527=00 | | | | | | |

IST & Final Bill.

Audited & Admitted for Rs. 10247000=00

9721527=00 by Cheque

and Rs. 525473=00 by adjustement

Accts. Supdt.
Yelahanka Division
BBMP

Exe. Engineer
Yelahanka Division
BBMP
